

Iteration Report: Iteration 1

By Guild Board

Chosen Irl Challenge: **Project D:** Course Support & Activity Dashboard



Project D: COURSE SUPPORT & ACTIVITY DASHBOARD

Picha Wiwattanawongsa	6610545430
Prima Xivivadh	6610545332
Navin Bunthuphanich	6610545251
Phasathat Jaruchitsophon	6610545375


Table of Contents

1. Project Snapshot.....	3
1.1 Project Wide Gantt Chart.....	3
1.2 Current Iteration Gantt Chart.....	4
2. Sprint / Board Status Snapshot.....	5
3. Scope Addition / Change log.....	6
4. Retrospective.....	6
5. Testing & Quality Notes.....	6
6. Project Risk Register.....	7
7. Individual Contribution Log.....	8

1. Project Snapshot

Project Repository: WIP


1.1 Project Wide Gantt Chart

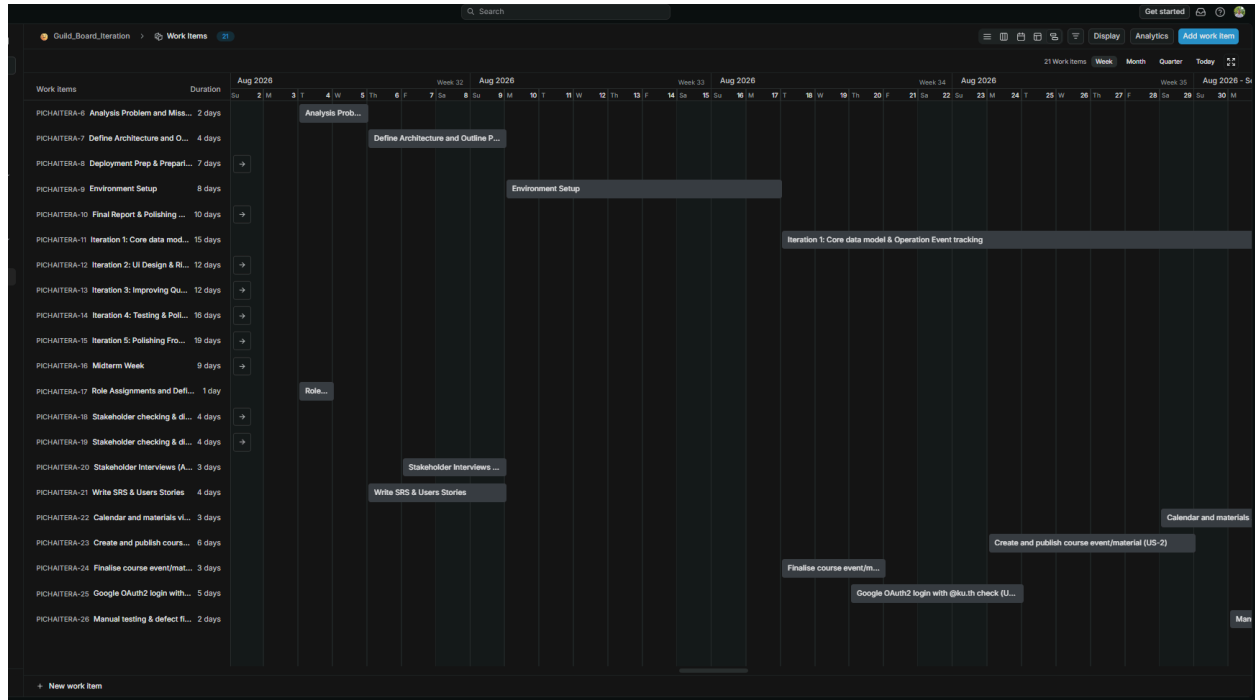

Critical Path: Role Assignments and Define Role Assignments → Analysis Problem and Mission → Stakeholder Interviews (Aj. Milk and TA) / Write SRS & User Stories / Define Architecture and Outline Proposal (done in parallel) → Environment Setup → Iteration 1: Core data model & Operation Event tracking → Iteration 2: UI Design & Risk Management → Midterm Week → Iteration 3: Improving Quality & Polishing Report & Proposal → Stakeholder checking & discussing feedback 2 → Iteration 4: Testing & Polishing Back-end → Iteration 5: Polishing Front-end & Debugging → Deployment Prep & Preparing Presentation Guide & Document → Final Report & Polishing & Rehearsal Presentation

Critical Path Duration: 120 calendar days

1.2 Current Iteration Gantt Chart

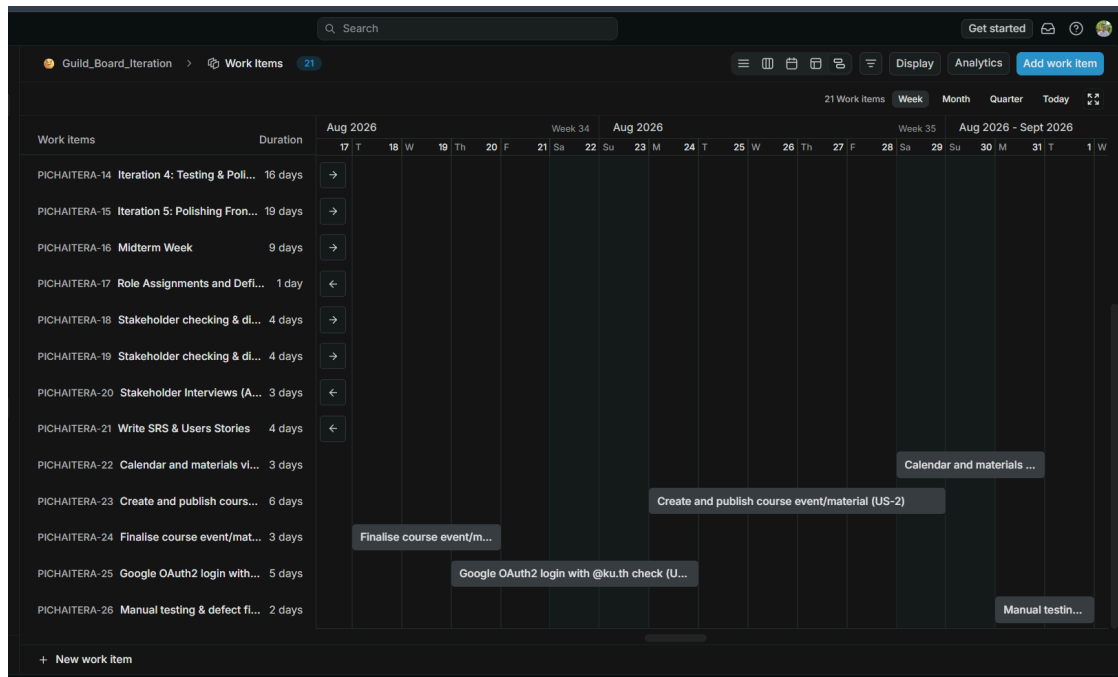

Critical Path: Finalise course event/material data model → Google OAuth2 login with @ku.th check (US-6) → Create and publish course event/material (US-2) → Calendar and materials view (US-1) → Manual testing & defect fixes

Critical Path Duration: 14 calendar days

2. Sprint / Board Status Snapshot

Note:

Iteration Goal: Get a working slice of the dashboard that we can demo. A staff member signs in with their @ku.th account, publishes a course event or material, and students and TAs can see it on the calendar. This covers SG-1 and sets up the login and data model that every other feature needs later.

Capacity Declared: 3 user stories (Iteration 1 hard limit, so no other basis needed).

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-1	As a student I want to view the course calendar and materials so that I know the upcoming deadlines and always have an updated study plan	Prima Xivivadh	Done	Y	Had to wait for US-2 to get test data. Shows only the latest published version (SRS-1, SRS-2)
US-2	As a lecturer I want to create and update course events and materials so that students and TAs are informed with up-to-date and accurate information	Picha Wiwattanawongsa	Done	Y	Main blocker story. Required fields are checked (SRS-4, SRS-5)
US-6	As a TA or Lecturer, I want to log in using my KU Google account so that only authorised department staff (@ku.th) can access the system	Navin Bunthuphanich	Done	Y	Domain check works (SRS-12). Full role permissions are not done yet, moved to Iteration 2

3. Scope Addition / Change log

Item added/changed	Reason	What as dropped to compensate (one-in-one-out)
(None applicable)	We stuck to the 3 stories we committed to at planning	(None)

4. Retrospective

What went well	What didn't go well	Action items for next sprint
We agreed on the event/material data model in the first few days, so US-1 and US-2 could start early	Setting up Google OAuth2 took longer than we thought because we had to set up the Google Cloud project and consent screen first	Put external setup work in Plane.so as its own task instead of hiding it inside a story
Having the traceability table from the SRS made it easy to check when a story was actually finished	We only built enough access control to demo US-2. The full Lecturer/TA/Admin permission part (SRS-3, SRS-8) is still missing	Give the permission matrix its own time slot in Iteration 2, not as an add-on to a feature
Daily short check-ins kept everyone on the same task each day	We only have 4 people, so one person ended up doing both testing and all the report/Gantt work near the deadline	Swap the testing and PM role next iteration so it is not always the same person

5. Testing & Quality Notes

We tested all three stories manually.

For US-2, we tried saving an event without a title, without a type, and without a date/time. All three failed to save and showed an error message, which is what SRS-4 and SRS-5 ask for.

For US-1, we checked the calendar against the seeded data. Only published items showed up, and each one showed title, type, date/time and owner (SRS-1, SRS-2).

For US-6, we tried logging in with a @ku.th account and with a normal Gmail account. The Gmail one was blocked with an error message (SRS-12).

Keeping old versions of materials is not implemented yet, only the latest published one, so that is left for a later iteration.

One bug found and fixed: after editing an event, the student calendar still showed the old version. It was a missing commit call in the update function.

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/Contingency	Status
R-01	Login depends on Google OAuth2, which is outside our control. If the Google Cloud config or consent screen breaks, nobody can get into the system at all	M	H	Keep the login code separate from the rest of the app, and keep a local test account so we can still develop and demo	Monitoring
R-02	The event/material schema might need rework later when at-risk flagging (SRS-7) and search (SRS-13, SRS-14) need tickets, events and materials queried together	M	H	Keep the schema loosely coupled and do not hardcode things that would block foreign keys or a shared search later	Open
R-03	None of us has done this process before, so our self-declared capacity for Iteration 2 might be wrong. With only 4 members, one person missing is a quarter of the team	M	M	Record how long each story actually took this iteration to use as a baseline, and pair up on critical path stories so no story has only one person who understands it	Open

7. Individual Contribution Log

Student name	Task Owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
R-01	Picha Wiwattanawongsa	Course event/material data model; US-2 (create and publish event/material)	Table mapping from the database lecture, CRUD for the create/update operation, validation flow taken from AD-1	5
R-02	Prima Xivivadh	US-1 (calendar and materials view), frontend and queries	Traceability from URS-1/URS-2 to SRS-1/SRS-2 when mapping fields to the UI, read-only flow from AD-2	5
R-03	Navin Bunthuphanich	US-6 (Google OAuth2 login) and the @ku.th domain check	Authorisation check and security layer from the architecture lecture, flow followed from SQD-7	4
R-04	Phasathat Jaruchitsophon	Gantt chart and critical path for the Project Snapshot, manual testing across all stories, bug logging	Critical path method from the Week 2 lecture, informal testing against the acceptance criteria in the SRS	4
